




The City of **WORCESTER**

Department of Public Works & Parks

Engineering Division Construction Progress Report

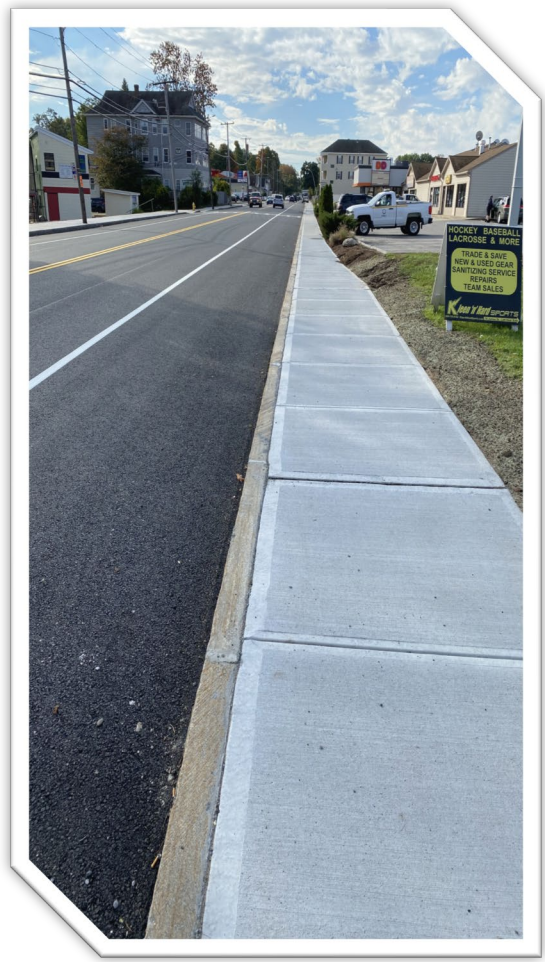

2022 - South Ludlow St - Between James Street and City Line
Road & Sidewalk Reconstruction (before and After)

Month Ending: October 31, 2022

Submitted by: _____

Jay J. Fink, P.E.

Commissioner of Public Works & Parks

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
1	Amherst Street	Between Kinnicutt Rd. & Winifred Ave.	Street Resurfacing 2022-2023	0%
1	Bay State Road	Brighton Rd. to Thorndyke Rd.	Street Resurfacing 2023-2024	0%
1	Bay State Road	Devens Rd. to Ontario St.	Street Resurfacing 2023-2024	0%
1	Bay State Road	Squantum St. to Brighton Rd.	Street Resurfacing 2023-2024	0%
1	Barry Road	Salisbury St. to Dick Dr.	Street Resurfacing 2023-2024	0%
1	Barry Road Ext.	Barry Rd to West Chester St.	Street Resurfacing 2022	100%
1	Bellingham Road	Vicinity 38	Sidewalk Reconstruction	0%
1	Brattle Street	Holden St. to Ararat St.	Street Resurfacing 2022	100%
1	Brandon Road	Wahnita Rd. to Fairhaven Rd.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Burncoat Street	East Mountain St. to 1645' N. of East Mountain St.	Street Resurfacing 2022	100%
1	Calumet Avenue	Clark St. to Monomoy St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Calumet Avenue	Squantum St. to Monomoy St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Castine Street	Dixfield St. to SW End	Street Resurfacing 2023-2024	0%
1	Chalmers Road	In front of #16	Repair around manholes	0%
1	Chester Street	Holden St. to Grove St.	Street Resurfacing 2022	100%
1	Chester Street	Russell Calvin Dr. to Chester Ter.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
1	Chester Street	W. Chester St. to Parkton Ave.	Street Resurfacing 2022-2023	0%
1	Darrow Street	South End to Aphorp St.	Street Resurfacing 2023-2024	0%
1	Dorothy Avenue	Burncoat St. to Hillcroft Ave.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Drury Lane	Massachusetts Av.e to Rutland Ter.	Street Resurfacing 2023-2024	0%
1	Eagle Road	Apollo Rd to South End	Street Resurfacing 2023-2024	0%
1	Eagle Road	Grove St. to Waycross St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Eagle Road	Waycross St. to Neptune Rd.	Street Resurfacing 2023-2024	0%
1	Ellis Drive	Winifred Ave. to Southwood Rd.	Street Resurfacing 2023-2024	0%
1	Flagg Street	Berwick St. to Hanna Rd.	Street Resurfacing 2023-2024	0%
1	Florida Avenue	Brookman St. to West End	Street Resurfacing 2023-2024	0%
1	Great Brook Valley Drive	Tacoma St. to Brookview Dr.	Street Resurfacing 2023-2024	0%
1	Hillcroft Avenue	Dorothy Ave. to Jeppson Ave.	Street Resurfacing 2023-2024	0%
1	Hillcroft Avenue	Jeppson Ave. to Cutting Ave.	Street Resurfacing 2023-2024	0%
1	Hillcroft Avenue	King Philip Rd. to Whitmarsh Ave.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
1	Inwood Road	Burncoat St. to Quinapoxet Ln.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	98%
1	Kalmar Street	Kalmar (Wb) St. to Fraternal Ave.	Street Resurfacing 2023-2024	0%
1	Kalmar (EB) Street	108' E of Fraternal Ave. to 616' E of Fraternal Ave.	Street Resurfacing 2022-2023	100%
1	Katahdin Street	Wilbur St to North End	Street Resurfacing 2023-2024	0%
1	Marmion Avenue	Wilkinson St. to Blue Hill Rd.	Street Resurfacing 2023-2024	0%
1	Massachusetts Ave	Vicinity 8	Sidewalk Reconstruction	100%
1	Matteo Street	Allison Cir. to Adelaide Cir.	Street Resurfacing 2023-2024	0%
1	Midland Street	Creswell Rd. to Intervale Rd.	Street Resurfacing 2023-2024	0%
1	Navajo Road	Cheyenne Rd. to Marconi Rd.	Street Resurfacing	100%
1	Nelson Park Drive	Nelson P. to Deborah Rd.	Street Resurfacing 2023-2024	0%
1	Newton Avenue North	Amherst St. to Salisbury St.	Street Resurfacing 2023-2024	0%
1	Newton Avenue North	Amherst St. to Salisbury St.	Sewer Reconstruction	60%
1	Newton Avenue North	Midland St. to Suburban Rd.	Street Resurfacing 2023-2024	0%
1	Nottingham Road	Forest St. to Laconia Rd.	Street Resurfacing 2022 - 2023	0%
1	Oneida Avenue	Governors St. to SE End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	98%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
1	Orlando Avenue	Brookman St. to W End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
1	Osceola Avenue	Clark St to Squantum	Street Resurfacing 2022-2023 - ARPA Revenue 2022	98%
1	Otsego Road	Monadnock Rd. W & N to Forest St.	Street Resurfacing 2022	100%
1/2	Park Avenue	Institute Rd. to Gold Star Blvd.	Street Resurfacing 2022-2023	0%
1/2	Park Avenue	Grove St. to Salisbury St.	Street Resurfacing 2022-2023	45%
1	Pasadena Parkway	Tacoma St. to SE End	Street Resurfacing 2023-2024	0%
1	Piehl Avenue	Abby St. to SW End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Piehl Avenue	Holden St. to Abby St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Piehl Avenue	Holden St. to SW End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Pine Tree Lane	Vicinity 10	Sidewalk Reconstruction	0%
1	Quinapoxet Lane	Housatonic St. to Ascadilla Rd.	Street Resurfacing 2023-2024	0%
1	Radcliffe Street	Mountain St. W to Hunnewell Rd.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
1	Romola Road	Apollo Rd. to Balder Rd.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
1	Romola Road	Balder Rd. to Neptune Rd.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Romola Road	Hapgood Rd. to Kaness Crossing	Street Resurfacing 2022-2023	0%
1	Romola Road	Neptune Rd. to Hapgood Rd.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Romola Road	South End to Apollo Rd.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
1	Sagamore Road	Whitman Rd. to Monadnock Rd.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
1	Service Road	Great Brook Valley Ave. to Brookview Dr.	Street Resurfacing 2023-2024	0%
1	Service Road	Tacoma St. to Great Brook Valley Ave.	Street Resurfacing 2022-2023	0%
1	Smith Lane	Holden St. to West End	Street Resurfacing 2022	100%
1	Sunrise Avenue	Sunrise Ave Ext to NE End	Street Resurfacing 2023-2024	0%
1	Volkmar Road	19 Croydon Rd. N to 820 West Boylston St.	Street Resurfacing 2022-2023	Awaiting Water Work
1	West Mountain St.	#236 to West Boylston St.	Street Resurfacing	MassDot In Design
1	Wheeler Avenue	Vicinity 3	Sidewalk Reconstruction	0%
2	Assonet Street	Gold St. to Madison St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2	Ayrshire Road	Coburn St. to Lake Ave.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
2	Bates Avenue	441 Lincoln St to 485' S of Lincoln St	Street Resurfacing 2022	98%
2	Belmont Street	Lincoln St to Rte. 290	Street Resurfacing 2022-2023	0%
2	Benedict Road	258 Plantation St to Ancona Rd.	Street Resurfacing 2022-2023	0%
2	Berkeley Street	Eastern Ave. to Shamrock St.	Street Resurfacing 2022	95%
2	Boardman Street	Merrill St. Southerly #17	Sewer Rehab	100%
2	Bowditch Drive	Plantation St. to NE End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
2	Breck (#1) Street	Everard St. to East End	Street Resurfacing 2022-	80%
2	Breck (#1) Street	Rodney St. to Everard St.	Street Resurfacing 2022-	80%
2	Caprera Road	Adams St. to Imperial Rd.	Street Resurfacing 2023-2024	0%
2	Caprera Road	Imperial Rd. to Grandby Rd.	Street Resurfacing 2023-2024	0%
2/3	Delmont Avenue	Entire - Grafton St. to Hamilton St.	Private Street Conversion	95%
2	Dupont Street	Thorne St. to Hamilton St.	Street Resurfacing 2022-2023	0%
2	East Park Terrace	NE End to Oleum Ct.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
2	Eastern Avenue	Berkeley St. to Prospect St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
2	Edgeworth Street	Dryder St. to Milton St.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
2	Edward Street	Palmer St. to Earle St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2/4	Francis J. McGrath	At Franklin St.	Bridge Rehab & Bikeway	MassDot 90%
2	Franklin Street	Angela Rose Ln. to Pollock St.	Street Resurfacing 2023-2024	0%
2/3	Grafton Street	Washington Sq. to Rice Sq.	Street Resurfacing 2022	MassDot 95% In Construction
2/4	Green Island Blvd.	Madison St. to Lamartine St.	Street Resurfacing 2022	100%
2	Green Street	#152	Sidewalk Reconstruction	0%
2	Green Street	#152	Sidewalk Reconstruction	0%
2	Green Street	N. of RR Bridge to Madison	Street Resurfacing	100%
2	Harrison Street	Green St. to Water St.	Street Resurfacing 2022	0%
2	Hastings Avenue	Boyd St. to Proctor St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2	Hastings Avenue	Tower St. to Boyd St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2	Hermitage Lane	50 Channing St. to Green St.	Street Resurfacing 2022	0%
2	Hospital Drive	Belmont St. to Dorista Goldsberry Drive	Sewer/Water Construction	70%
2	Hospital Drive	Belmont St. to Clock Tower Drive	Street Resurfacing 2022-2023	90%
2	Huntington Avenue	Proctor St. to Alexander Rd.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
2	Indian Lake Parkway	North Bound	Street Resurfacing 2023-2024	0%
2	Indian Lake Parkway	South Bound	Street Resurfacing 2023-2024	0%
2	Kendall (#2) Street	Goldsberry St. to East End	Street Resurfacing 2022-	0%
2	Kenwood Avenue	Ashburnham Rd. to West End	Street Resurfacing 2023-2024	0%
2/4	Lamartine Street	Millbury St. to Lodi St.	Street Resurfacing 2022	98%
2	Locust Avenue	Belmont St. to Wigwam Ave.	Street Resurfacing 2022-2023	60%
2	Main Street	Austin Street to Chandler St.	Downtown Streetscape	100%
2	Millbrook Street	At Burncoat St.	Signal Improvements	0%
2	Old Lincoln Street	Lincoln (NB) St. to Lincoln (NB) St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2	Paine Street	Norton St. to North End	Street Resurfacing 2023-2024	0%
2	Perkins Street	Paine St. to Lincoln (SB) St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	70%
2	Perkins Street	Lincoln (SB) St. to Lincoln St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2	Plymouth Street	Green St. to Summit St.	Street Resurfacing	100%
2	Rockport Road	Duxbury Rd. to Shattuck St.	Street Resurfacing 2023-2024	0%
2	Russell Street	Highland St. to Park Ave.	Sidewalk Reconstruction	80%
2	Sears Island Drive	Entire	Sidewalk Reconstruction	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
2	Trinity Avenue	Lincoln St. 214' SE of Colby St.	Street Resurfacing 2022	Awaiting Water Work
2	Vinson Street	Olga Ave. to End	Street Resurfacing 2023-2024	0%
2	Vinson Street	West End to East End	Street Resurfacing 2023-2024	0%
2	Wachusett Street	Highland St. to Institute Rd.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2	Westminster Street	Mountain Vernon St. to Forestdale Rd	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2	Windsor Street	Green Hill Pkwy to Sturgis St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
2	Windsor Street	Forbes St. to Orne St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	80%
3	Acton Street	Vale St. to Rice Ln.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
3	Aetna Street	Mendon St. to Cutler St.	Street Resurfacing 2022	100%
3	Alamo Street	5 Lamar Ave E to End	Street Resurfacing 2022-2023	100%
3	Bridgeport Street	88 Granite St. to Taunton St.	Street Resurfacing 2022-2023	0%
3	Cargill Avenue	168 Vernon NW to Strathmore Rd.	Street Resurfacing 2022-2023	0%
3	Dearborn Street	Crowningshield Rd. to Derby St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
3	Derby Street	Dearborn St. to West End	Street Resurfacing 2023-2024	0%
3	Fifth Avenue	Millbury St. to Gediminas St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
3	Forsberg Street	Harwich St. to West End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
3	Grafton Street	At Route 20	Bridge Rehab	MassDot
3	Houghton Street	Crowningshield Rd. to Derby St.	Street Resurfacing 2023-2024	0%
3	Lund Street	70 Esther W to Louise St.	Street Resurfacing 2022-2023	0%
3	Pinecrest Drive	Crestlan Cir. to Crestlan Dr.	Street Resurfacing 2023-2024	0%
3	Pinecrest Drive	Crestlan Dr. to Westborough St.	Street Resurfacing 2023-2024	0%
3	Pinecrest Drive	NE End to Crestlan Cir.	Street Resurfacing 2023-2024	0%
3	Plantation Street	Vicinity 9	Handicap Ramp	0%
3	Revere Street	Trahan Ave. W to Warner	Street Resurfacing 2022	95%
3	Rice Lane	Dorchester St. to Acton St.	Street Resurfacing 2022-2023	90%
3	Sandra Drive	Dolly Dr. to NW End	Street Resurfacing 2023-2024	0%
3	Sandra Drive	Ida Rd. to Dolly Rd.	Street Resurfacing 2023-2024	0%
3	Salford Street	108 Houghton W to 93 Vale	Street Resurfacing 2022	90%
3	Standish Street	Ida Rd. to Dolly Rd.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
3	Standish Street	Ida Rd. to Dolly Rd.	Street Resurfacing 2023-2024	0%
3	Standish Street	Ida Rd. to Dolly Rd.	Street Resurfacing 2023-2024	0%
3	Sterling Street	Hillside St. to View St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
3	Upland Street	Arboretum Dr. to SW End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
3	Upsala Street	Vicinity 36	Grind Curb & Ramp	0%
3	Upsala Street	Vicinity 36	Street Resurfacing	0%
3	Vale Street	Aetna St. to Dorchester St.	Street Resurfacing 2023-2024	0%
3	Vernon Terrace	53 Vernon E to End	Water Construction 2022-2023	100%
3	Vernon Terrace	53 Vernon E to End	Street Resurfacing 2022-2023	35%
3	Winnipeg Street	#8 to St. Louis St.	Sewer Reconstruction	95%
4	Armory Street	On Armory St. @ 154 Grand St.	Sidewalk Reconstruction	0%
4	Chandler Street	At Main & Irving St.	Intersection Improvements	MassDot Under Design
4	Chandler Street	At Main & Irving St.	Street Resurfacing	MassDot Under Design
4	Dewey Street	West Oberlin St. to Charlotte St.	Street Resurfacing 2023-2024	0%
4	Ethan Allen Street	92 Murray Ave to Jaques Ave.	Street Resurfacing 2022-2023	Awaiting Water Work
4	Endicott Street	Vernon St. to Harding Rd	Street Resurfacing	100%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
4	Freeland Terrace	Freeland St to Lowell Ct	Street Resurfacing 2022-2023	0%
4	Gardner Street	Canterbury St. to Southgate St.	Street Resurfacing 2022-2023	40%
4	Gardner Street	Canterbury St. to Girls & Boys	Road Lowering	20%
4	Grand Street	Albert St. to Hollis St.	Street Resurfacing 2023-2024	0%
4	Grand Street	Cheney St. to Albert St.	Street Resurfacing 2023-2024	0%
4	Grand Street	Cristy St. to Cheney St.	Street Resurfacing 2023-2024	0%
4	Grand Street	Hollis St. to Illinois St.	Street Resurfacing 2023-2024	0%
4	Grand Street	Illinois St. to SE End	Street Resurfacing 2023-2024	0%
4	Grand Street	Main St. to Cristy St.	Street Resurfacing 2023-2024	0%
4	Hermon Street	Southbridge St. to Gold St.	Street Resurfacing	MassDot 95% In Contract
4	Ionic Avenue	Main St. to Beacon St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	80%
4	Irene Street	Main St. to NW End	Street Resurfacing 2023-2024	0%
4	Jackson Street	Beacon St. to Lagrange St.	Street Resurfacing 2023-2024	0%
4	Jackson Street	Lagrange St. to Southbridge (#1) St.	Street Resurfacing 2023-2024	0%
4	Jackson Street	Main St. to Beacon St.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
4	Lafayette (#2) Street	Bigelow St. to Lodi St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
4	Lafayette (#2) Street	Scott St. to Washington St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
4	Lafayette (#2) Street	Washington St. to Harding (SB) St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
4	Main Street	Richard St. to Hancock St.	Street Resurfacing	Mass Dot 95% In Construction
4/5	Park Avenue	May St. to Lovell St.	Street Resurfacing 2022-2023	0%
4	Pitt Street	Cambridge St. to Mitchell St.	Sidewalk Reconstruction	0%
4	Quincy Street	89 Chatham St. to 112 Austin	Street Resurfacing 2022	100%
4	Sargent Street	Gold St. to SE End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
4	Sargent Street	Southbridge (#1) St. to Gold St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
4	Sigel Street	Millbury (NB) St. to Harding (SB) St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
4	Stone Street	South Ward St. to Perry Ave.	Street Resurfacing 2023-2024	0%
4	Stoneland Road	Main St. to Haynes St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
4	Ward Street	Stone St. to 363' S to Vernon St.	Street Resurfacing 2022-2023	100%
4	Ward Street	Stone St. to 363' S to Vernon	Sewer Reconstruction	100%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
4	Washington Street	Lamartine St. to Madison St.	Street Resurfacing	100%
4	West Street	John St. to Dayton St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	40%
4	Winslow Street	Larch St. to Austin St.	Street Resurfacing 2023-2024	0%
4	Winslow Street	Pleasant St. to Larch St.	Street Resurfacing 2023-2024	0%
4	Woodland Street	Vicinity 54	Utility Repair	0%
5	Bauer Street	Main St. to Farmington St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Bauer Street West	Farmington St. to Mildred Ave.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Bauer Street West	Mildred Ave. to Ludlow (#1) St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Beeching Street	Vicinity 97	Sidewalk Reconstruction	100%
5	Brantwood Road	Vicinity 70-72	Sidewalk Reconstruction	On Hold per
5	Briarcliff Street	Beaconsfield Rd. to West End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
5	Brookshire Road	Santuit Ln. to Oak Hill Rd.	Street Resurfacing 2023-2024	0%
5	Buckley Road	#20 to #37	Street Resurfacing 2022-2023	0%
5	Catalpa Street	Catalpa Cr. To Montague St.	Street Resurfacing 2022-2023	Awaiting Water Work
5	Chesterfield Road	Beaconsfield Rd. to Pleasant St.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
5	Circuit Ave North	Circuit Ave. East to Vincent Ave.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Clegg Street	Great Post Rd. to Apricot St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
5	Crest Circle	Wildwood Ave. S to 838' E of Wildwood Ave.	Street Resurfacing 2022	100%
5	Edwidge Street	Pleasant St. to North End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Eureka Street	Colrain St. to Abington (#2) St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
5	Fielding Street	West End to East End	Street Resurfacing 2023-2024	0%
5	Great Post Road	Main St. to Clegg St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
5	Hadwen Lane	784 Pleasant S & W to 85 Morningside Rd.	Street Resurfacing 2022	0%
5	Hadwen Lane	Westview Rd. to Perrot St.	Street Resurfacing 2022-	0%
5	Hamill Road	May St. to Chandler St.	Street Resurfacing 2022-	0%
5	James Street	Stafford St. to Ludlow St.	Street Resurfacing 2022-2023	100%
5	Laurelwood Drive	Pleasant St. to South End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Longfellow Road	Commodore Rd. to Copley Rd.	Street Resurfacing 2023-2024	0%
5	Longfellow Road	Coolidge Rd. to Commodore Rd.	Street Resurfacing 2023-2024	0%

<u>DISTRICT</u>	<u>STREET</u>	<u>LIMITS</u>	<u>TYPE OF WORK</u>	<u>% COMPLETE</u>
5	Longfellow Road	Coply Rd. to Coolidge Rd.	Street Resurfacing 2023-2024	0%
5	Ludington Road	June St. to North End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
5	Manhattan Road	Chandler St. to Rydal St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
5	Minthorne Street	Clive St. to Circuit Ave. North	Street Resurfacing 2023-2024	0%
5	Monticello Drive	Brookline St. to Wyola Dr.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
5	Moore Avenue	Pleasant St. to End	Street Resurfacing 2022-2023	Awaiting Water Work
5	Moreland Green	2082' W of Moreland St.	Street Resurfacing	100%
5	Nevada Street	Nevada Street Side of 43 June St.	Sidewalk Reconstruction	100%
5	Northbridge Street	May St. to South End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Parker Street	Winfield (#1) St. to Mayfield St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%
5	Reed Street	Courtland St. to Norcross St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Reed Street	Norcross St. to Geneva St.	Street Resurfacing 2022-2023 - ARPA Revenue 2022	0%
5	Rockwood Avenue	Pleasant St. to North End	Street Resurfacing 2022-2023 - ARPA Revenue 2022	100%

